

Resource Management Agency COUNTY OF TULARE AGENDA ITEM

BOARD OF SUPERVISORS

KUYLER CROCKER District One

PETE VANDER POEL District Two

AMY SHUKLIAN District Three

EDDIE VALERO District Four

DENNIS TOWNSEND

AGENDA DATE: February 26, 2019

Г

Public Hearing Required	Yes 🗌 N/A 🖂
Scheduled Public Hearing w/Clerk	Yes 🗌 N/A 🖾
Published Notice Required	Yes 🗌 N/A 🖾
Advertised Published Notice	Yes 🗌 N/A 🖾
Meet & Confer Required	Yes 🗌 N/A 🖾
Electronic file(s) has been sent	Yes 🛛 N/A 🗌
Budget Transfer (Aud 308) attached	Yes 🗌 N/A 🖾
Personnel Resolution attached	Yes 🗌 N/A 🖾
Agreements are attached and signature	line for Chairman is marked with
tab(s)/flag(s)	Yes 🛛 N/A 🗌
CONTACT PERSON: Celeste Perez PHO	NE: 559-624-7010

SUBJECT: Notice of Completion for Construction of the 2018 Road Repair and Accountability Act (RRAA) Project 1

REQUEST(S):

That the Board of Supervisors:

- 1. Accept the work for the construction of the 2018 Road Repair and Accountability Act (RRAA) Project 1 as complete by Agee Construction Corporation of Clovis, California; and
- 2. Authorize the Chairman to sign the Notice of Completion; and
- 3. Direct the Clerk of the Board to have the Notice of Completion recorded with the County Recorder.

SUMMARY:

This Notice of Completion is for the construction of the 2018 Road Repair and Accountability Act (RRAA) Project 1. This project was completed on schedule and within the allowable budget. The work was performed by Agee Construction Corporation under Tulare County Agreement No. 28502.

This project was approved by your Board on January 9, 2018 (Resolution No. 2018-0029). The lowest responsible bid was submitted by Agee Construction Corporation. On March 13, 2018, your Board awarded and approved (Resolution No. 2018-0173) a contract with Agee Construction Corporation of Clovis, California in the amount of \$3,041,556.

SUBJECT:Notice of Completion for Construction of the 2018 Road Repair and
Accountability Act (RRAA) Project 1DATE:February 26, 2019

This project consisted of a combination of isolated pavement repairs followed by the installation of new asphalt surfacing, as well as full depth pulverization of existing asphalt material followed by the application of new asphalt surfacing.

Provided below is a summary of the roadway which received treatment as part of this project:

- Avenue 408 from Road 112 to Road 120
- Avenue 384 from Road 80 to Road 96
- Avenue 264 from State Route 99 to Road 100
- Road 100 from Avenue 264 to Avenue 276
- Road 158 from Avenue 296 to State Route 216
- Avenue 368 from Road 100 to Road 108

There were two Contract Change Orders (CCO) written for this project, with a net total savings to the County of \$1,731.65. The first CCO, in the net amount (credit to the County) of \$1,731.65, was written to compensate the contractor as set forth in the "Payment Adjustment for Price Index Fluctuations" clause of the Special Provisions and to credit the County for asphalt material outside of the allowable density range, but within contract acceptance, as specified in the project specifications. The second CCO was a zero-dollar change order to allow contract items to exceed the 125% threshold without the need to provide an adjustment to the contract item unit price.

An allowance of 5.41% of the contract bid amount, or \$164,577, was authorized for contingencies at the time of award setting the total approved contract amount at \$3,206,133.

The final project cost to complete this project was \$3,043,884.87 which is 0.08% above the bid amount and is 5.06% below the authorized contract amount plus contingencies.

This project has been completed in accordance with the plans and specifications and is now ready for acceptance by the Board.

FISCAL IMPACT/FINANCING:

No Net County Cost.

Contract Bid Amount:	\$ 3,041,556.00
5.4% of amount authorized for Contingencies:	<u>\$ 164,577.00</u>
Authorized Contract Bid Amount + Contingencies:	\$ 3,206,133.00
Project Cost:	\$ 3,045,616.52
Total Cost of Contract Change Orders:	<u>\$ (1,731.65)</u>
Final Project Cost:	\$ 3,043,884.87

SUBJECT:Notice of Completion for Construction of the 2018 Road Repair and
Accountability Act (RRAA) Project 1DATE:February 26, 2019

An allowance of 5.41% of the contract bid amount, or \$164,577, was authorized for contingencies at the time of project approval setting the total approved contract amount at \$3,206,133.

The final project cost to complete this project was \$3,043,884.87 which is 0.08% above the bid amount and is 5.06% below the authorized contract amount plus contingencies.

This project was fully funded by the roads fund with revenue coming from the State Road Maintenance and Rehabilitation Account (RMRA), Local Measure R, and other State and Federal roads funding sources.

LINKAGE TO THE COUNTY OF TULARE STRATEGIC BUSINESS PLAN:

This project will enhance the safety and security of the public by improving the transportation infrastructure for both the general population in the region and the motorists using this facility.

ADMINISTRATIVE SIGN-OFF:

Reed Schenke, P.E. Director

Attachment(s) Attachment A – Vicinity Map Attachment B – Notice of Completion

cc: County Administrative Office

BEFORE THE BOARD OF SUPERVISORS COUNTY OF TULARE, STATE OF CALIFORNIA

)

)

)

)

IN THE MATTER OF NOTICE OF COMPLETION FOR CONSTRUCTION OF THE 2018 ROAD REPAIR AND ACCOUNTABILITY ACT (RRAA) PROJECT 1) Resolution No. _____


UPON MOTION OF SUPERVISOR ______, SECONDED BY SUPERVISOR ______, THE FOLLOWING WAS ADOPTED BY THE BOARD OF SUPERVISORS, AT AN OFFICIAL MEETING HELD <u>FEBRUARY 26, 2019</u>, BY THE FOLLOWING VOTE:

AYES: NOES: ABSTAIN: ABSENT:

> ATTEST: JASON T. BRITT COUNTY ADMINISTRATIVE OFFICER/ CLERK, BOARD OF SUPERVISORS

- Accepted the work for the construction of the 2018 Road Repair and Accountability Act (RRAA) Project 1 as complete by Agee Construction Corporation of Clovis, California; and
- 2. Authorized the Chairman to sign the Notice of Completion; and
- 3. Directed the Clerk of the Board to have the Notice of Completion recorded with the County Recorder.

Attachment A – Vicinity Map

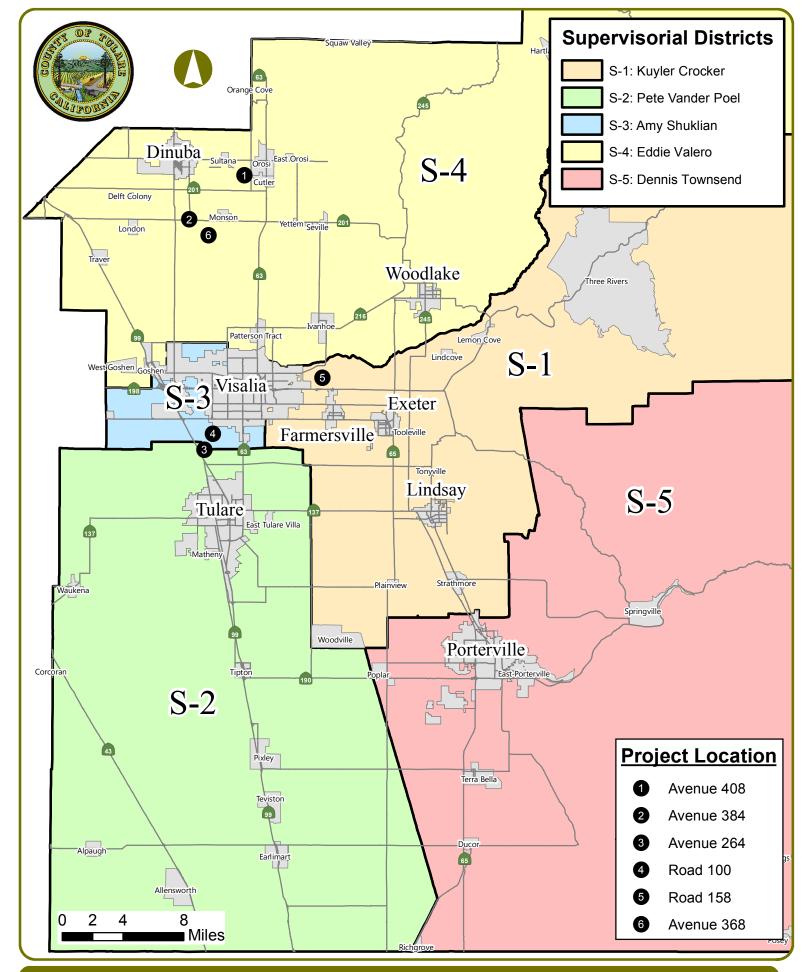

Attachment A - Project Location Map 2018 Road Repair and Accountability Act (RRAA) Project 1

Attachment B – Notice of Completion

NOTICE OF COMPLETION

NOTICE IS HEREBY GIVEN THAT:

- 1. The County of Tulare, a political subdivision of the State of California, is the owner of the work of improvement stated below.
- 2. The full address of the owner is: County of Tulare, 2800 W. Burrel Avenue, Visalia, California, 93291
- 3. The County of Tulare, a public agency, owns the hereinafter described work of improvement.
- 4. No other person(s) or corporation(s) owns any interest therein.
- 5. The name of the project is 2018 Road Repair and Accountability Act (RRAA) Project 1.
- 6. On the 26th day of February, 2019 the Board of Supervisors of Tulare County in Resolution Number accepted as complete the work of improvement in Tulare County Agreement Number 28502 for the project identified above.
- 7. The name of the contractor for the work of improvement described in Tulare County Agreement Number 28502 is Agee Construction Corporation. The Contractor's address is Agee Construction Corporation, P.O. Box 629, Clovis, California, 93613.
- 8. The project was located on the following locations: 1) Avenue 408 from Road 112 to Road 120, 2) Avenue 384 from Road 80 to Road 96, 3) Avenue 264 from State Route 99 to Road 100, 4) Road 100 from Avenue 264 to Avenue 276, 5) Road 158 from Avenue 296 to State Route 216, and 6) Avenue 368 from Road 100 to Road 108, County of Tulare, State of California.

The undersigned affirms that he is authorized to execute this Notice of Completion for the County of Tulare, that he has read the foregoing Notice, knows the contents hereof and that the facts stated herein are true; that he executes this Notice on behalf of and pursuant to the authorization of the Board of Supervisors of the County of Tulare.

> COUNTY OF TULARE **BOARD OF SUPERVISORS**

Chairman of the Board

A notary public or other officer completing this certificate verifies only the identity of the individual who signed the document to which this certificate is attached, and not the truthfulness, accuracy, or validity of that document.

State of California) County of Tulare

Subscribed	and	sworn	to (or	affirmed)	before	me	on	this _	day	of			, 2019	Э, by
					, proved	to me c	on th	ie ba	sis of	satisfactory	evidence t	to be t	the	person(s)	who
appeared be	efore	me.													

Date:

)

Notary Signature
