



**Resource Management
Agency
COUNTY OF TULARE
AGENDA ITEM**

BOARD OF SUPERVISORS

KUYLER CROCKER
District One
PETE VANDER POEL
District Two
AMY SHUKLIAN
District Three
EDDIE VALERO
District Four
DENNIS TOWNSEND
District Five

AGENDA DATE: January 14, 2020

Public Hearing Required	Yes	<input type="checkbox"/>	N/A	<input checked="" type="checkbox"/>
Scheduled Public Hearing w/Clerk	Yes	<input type="checkbox"/>	N/A	<input checked="" type="checkbox"/>
Published Notice Required	Yes	<input type="checkbox"/>	N/A	<input checked="" type="checkbox"/>
Advertised Published Notice	Yes	<input type="checkbox"/>	N/A	<input checked="" type="checkbox"/>
Meet & Confer Required	Yes	<input type="checkbox"/>	N/A	<input checked="" type="checkbox"/>
Electronic file(s) has been sent	Yes	<input checked="" type="checkbox"/>	N/A	<input type="checkbox"/>
Budget Transfer (Aud 308) attached	Yes	<input type="checkbox"/>	N/A	<input checked="" type="checkbox"/>
Personnel Resolution attached	Yes	<input type="checkbox"/>	N/A	<input checked="" type="checkbox"/>
Agreements are attached and signature line for Chairman is marked with tab(s)/flag(s)	Yes	<input type="checkbox"/>	N/A	<input checked="" type="checkbox"/>
CONTACT PERSON: Celeste Perez PHONE: (559)624-7010				

SUBJECT: Notice of Completion for Construction of Avenue 280 Widening Project

REQUEST(S):

That the Board of Supervisors:

1. Accept the work for the construction of the Avenue 280 Widening Project as complete by Cal Valley Construction, Inc. of Fresno, California; and
2. Authorize the Chairman to sign the Notice of Completion; and
3. Direct the Clerk of the Board to have the Notice of Completion recorded with the County Recorder.

SUMMARY:

This Notice of Completion is for the construction of the Avenue 280 Widening Project. This project overran allowable working time; however, the project was completed below the allowable budget. The work was performed by Cal Valley Construction, Inc. under Tulare County Agreement No. 28231.

This project was approved by your Board on April 18, 2017 (Resolution No. 2017-0246). The lowest responsible bid was submitted by Cal Valley Construction, Inc. On June 20, 2017, your Board awarded and approved a contract (Resolution No. 2017-0477) to Cal Valley Construction, Inc. of Fresno, California in the amount of \$10,051,865.68.

This project consisted of widening Avenue 280 to a four lane roadway with center median and turn lanes between State Route 99 and Road 100. This project also

SUBJECT: Notice of Completion for Construction of Avenue 280 Widening Project
DATE: January 14, 2020

included the installation of class 2 bike lanes, pedestrian facilities, street lighting, a traffic signal at Avenue 280 and Road 92, raised decorative concrete median treatments, and a new double box culvert crossing on Road 92. This 2-mile segment of Avenue 280 is the first phase of the overall project to widen approximately 11-miles of the Avenue 280 corridor.

There were fifteen Contract Change Orders (CCO) written for this project with a net total cost of \$332,573.12. The summary of the CCO's written for this project are summarized in Attachment C.

Work on this contract was completed seven (7) working days beyond the calculated date of completion. Since this contractor overran the number of working days authorized for the project, liquidated damages (LD) have been assessed. The penalty for LD for this project was set at \$8,300 per day; therefore, the total amount of LD assessed for this project is \$58,100.

This project has been completed in accordance with the plans and specifications and is now ready for acceptance by the Board.

FISCAL IMPACT/FINANCING:

There is No Net County cost.

Contract Bid Amount:	\$10,051,865.68
5.25% of amount authorized for Contingencies	\$ 515,093.00
Authorized Contract Bid Amount + Contingencies	\$10,566,958.68
Project Cost:	\$ 9,192,265.49
Total of Contract Changer Orders:	\$ 332,573.12
LD Withholdings 7 days @ \$8,300	\$ (58,100.00)
Final Project Cost:	\$ 9,466,738.61

An allowance of 5.12% of the contract bid amount, or \$515,093, was authorized for contingencies at the time of award setting the total approved contract amount at \$10,566,958.68.

The final cost to complete this project was \$9,466,738.61 which is 5.82% below the bid amount and is 10.41% below the authorized contract amount plus contingencies.


This project was fully funded through Measure R Regional Program funds.

LINKAGE TO THE COUNTY OF TULARE STRATEGIC BUSINESS PLAN:

Safety and Security – This project will enhance the safety and security of the public by improving the transportation infrastructure for both the general population in the region and the motorists using this facility.

SUBJECT: Notice of Completion for Construction of Avenue 280 Widening Project
DATE: January 14, 2020

ADMINISTRATIVE SIGN-OFF:



Reed Schenke, P.E.
Director

cc: County Administrative Office

Attachment(s) Attachment A – Vicinity Map
Attachment B – Notice of Completion
Attachment C – Change Order Summary

**BEFORE THE BOARD OF SUPERVISORS
COUNTY OF TULARE, STATE OF CALIFORNIA**

IN THE MATTER OF NOTICE OF)
COMPLETION FOR CONSTRUCTION OF) Resolution No. _____
AVENUE 280 WIDENING PROJECT)

UPON MOTION OF SUPERVISOR _____, SECONDED BY
SUPERVISOR _____, THE FOLLOWING WAS ADOPTED BY THE
BOARD OF SUPERVISORS, AT AN OFFICIAL MEETING HELD JANUARY 14, 2020,
BY THE FOLLOWING VOTE:

AYES:
NOES:
ABSTAIN:
ABSENT:


ATTEST: JASON T. BRITT
COUNTY ADMINISTRATIVE OFFICER/
CLERK, BOARD OF SUPERVISORS

BY: _____
Deputy Clerk

* * * * *

1. Accepted the work for the construction of the Avenue 280 Widening Project as complete by Cal Valley Construction, Inc. of Fresno, California; and
2. Authorized the Chairman to sign the Notice of Completion; and
3. Directed the Clerk of the Board to have the Notice of Completion recorded with the County Recorder.

**ATTACHMENT A –
VICINITY MAP**

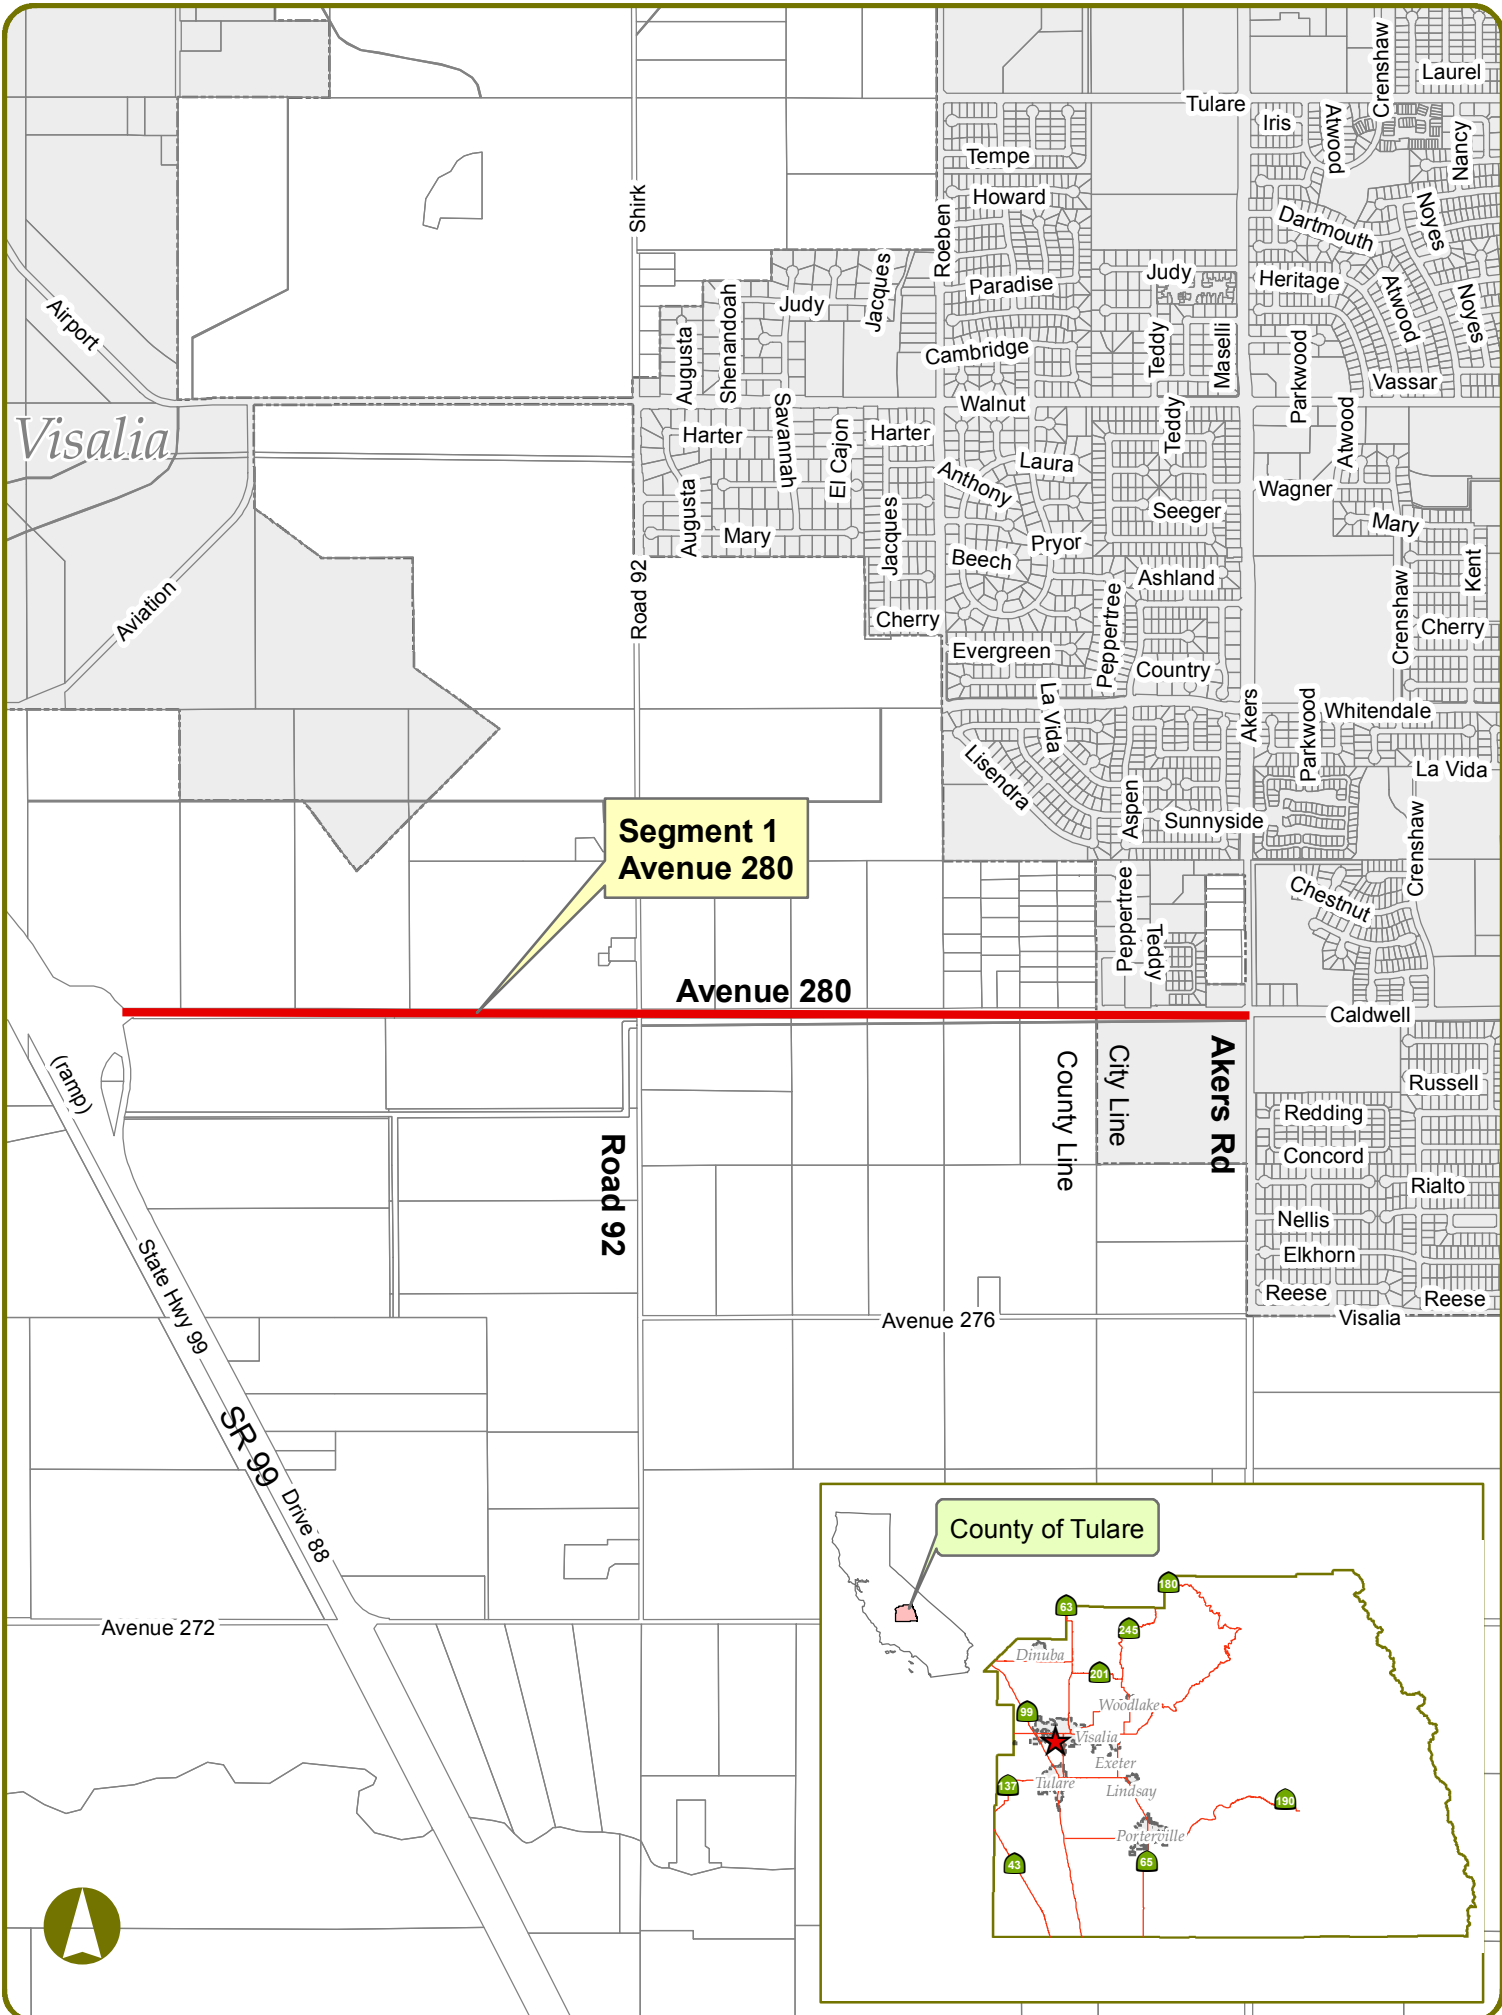

**Segment 1
Avenue 280**

Avenue 280

Akers Rd

County of Tulare

**ATTACHMENT B –
NOTICE OF COMPLETION**

When recorded return to:
Clerk of the Board
County of Tulare
2800 West Burrel
Visalia, CA 93291

NOTICE OF COMPLETION

NOTICE IS HEREBY GIVEN THAT:

1. The County of Tulare, a political subdivision of the State of California, is the owner of the work of improvement stated below.
2. The full address of the owner is: County of Tulare, 2800 W. Burrel Avenue, Visalia, California, 93291
3. The County of Tulare, a public agency, owns the hereinafter described work of improvement.
4. No other person(s) or corporation(s) owns any interest therein.
5. The name of the project is Avenue 280 Widening Project.
6. On the 14th day of January, 2020 the Board of Supervisors of Tulare County in Resolution Number _____ accepted as complete the work of improvement in Tulare County Agreement Number 28231 for the project identified above.
7. The name of the Contractor for the work of improvement described in Tulare County Agreement Number 28231 is Cal Valley Construction, Inc. The Contractor's address is Cal Valley Construction, Inc. 5125 N. Gates Avenue Suite 102, Fresno, California 93722.
8. The project was located just west of the City of Visalia along Avenue 280 between State Route 99 and Road 100, County of Tulare, State of California.

The undersigned affirms that he is authorized to execute this Notice of Completion for the County of Tulare, that he has read the foregoing Notice, knows the contents hereof and that the facts stated herein are true; that he executes this Notice on behalf of and pursuant to the authorization of the Board of Supervisors of the County of Tulare.

COUNTY OF TULARE
BOARD OF SUPERVISORS

Chairman of the Board

A notary public or other officer completing this certificate verifies only the identity of the individual who signed the document to which this certificate is attached, and not the truthfulness, accuracy, or validity of that document.

State of California)
County of Tulare)

Subscribed and sworn to (or affirmed) before me on this _____ day of _____, 2020, by _____, proved to me on the basis of satisfactory evidence to be the person(s) who appeared before me.

Date: _____

Notary Signature

**ATTACHMENT C –
CHANGE ORDER SUMMARY**

Change Order Summary

Avenue 280 Widening Project

Contract Change Order No. 1

Additional costs associated with the implementation of the Stage 2B Traffic Handling Plan.

Total cost for this CCO = \$198,097.00

Contract Change Order No. 2

Compensated the Contractor for removing and disposing 400 linear feet of 18-inch reinforced concrete pipe.

Total cost for this CCO = \$3,000.00

Contract Change Order No. 3

Compensated the Contractor for excavating saturated subgrade material from isolated areas.

Total cost for this CCO = \$23,000.00

Contract Change Order No. 4

Compensated the Contractor for modifying the proposed embankment on the south side of the Avenue 280 west of Shirk Road.

Total cost for this CCO = \$12,500.00

Contract Change Order No. 5

Compensated the Contractor for costs associated with the rental of 1,043 linear feet of temporary fencing utilized on the project.

Total cost for this CCO = \$17,000.00

Contract Change Order No. 6

Reimbursed the Contractor for making direct payment to Southern California Edison (SCE) to provide electrical service connections for the proposed traffic signal at Avenue 280 and Road 92 as well as the proposed street lighting.

Total cost for this CCO = \$15,513.62

Contract Change Order No. 7

Compensated the Contractor to furnish and install two (2) removable bollards at the multiuse trail west of Shirk Road and installing four (4) additional traffic loops at this intersection of Shirk Road.

Total cost for this CCO = \$4,180.00

Contract Change Order No. 8

Compensated the Contractor for the realignment of Evans Ditch.

Total cost for this CCO = \$19,175.00

Contract Change Order No. 9

Compensated the Contractor for assisting the Gas Company in lowering a 4-inch medium pressure gas pipeline West of Akers which was found to be within the proposed structural section of the new roadway.

Total cost for this CCO = \$5,575.00

Contract Change Order No. 10

Compensated the Contractor for costs associated with roadway grading and drainage swale revisions as well as the installation of 60 linear feet of 12-inch reinforced concrete pipe along Shirk Road.

Total cost for this CCO = \$11,817.00

Contract Change Order No. 11

Compensated the Contractor for costs associated with the removal and disposal of buried debris found throughout the course of the project.

Total cost for this CCO = \$16,718.00

Contract Change Order No. 12

Compensated the Contractor to furnish and install 219 linear feet of two (2) 3-inch PVC conduits for future signal at the Sequoia Gateway Drive.

Total cost for this CCO = \$11,544.50

Contract Change Order No. 13

Provided credit to the County as a result asphalt material that was determined to be outside project specifications.

Total cost for this CCO = (\$5,025.00)

Contract Change Order No. 14

Provided credit to the County for the elimination of (3) street light foundations.

Total cost for this CCO = (\$5,932.00)

Contract Change Order No. 15

Allowed contract items to exceed the 75% and 125% threshold in accordance with Section 9-1.06C.

Total cost for this CCO = \$0.00
