


BEFORE THE BOARD OF SUPERVISORS COUNTY OF TULARE, STATE OF CALIFORNIA

IN THE MATTER OF NOTICE OF)
 COMPLETION FOR CONSTRUCTION OF) Resolution No. 2018-0554
 THE TERRA BELLA & RICHGROVE ROAD)
 IMPROVEMENT PROJECT)

UPON MOTION OF SUPERVISOR ENNIS, SECONDED BY SUPERVISOR CROCKER, THE FOLLOWING WAS ADOPTED BY THE BOARD OF SUPERVISORS, AT AN OFFICIAL MEETING HELD JUNE 26, 2018, BY THE FOLLOWING VOTE:

AYES: SUPERVISORS CROCKER, VANDER POEL, SHUKLIAN, WORTHLEY,
 AND ENNIS
 NOES: NONE
 ABSTAIN: NONE
 ABSENT: NONE



ATTEST: MICHAEL C. SPATA
 COUNTY ADMINISTRATIVE OFFICER/
 CLERK, BOARD OF SUPERVISORS

BY: Mary Ronello
 Deputy Clerk

1. Accepted the work for the construction of the Terra Bella & Richgrove Road Improvement Project as complete by Agee Construction Corporation of Clovis, California; and
2. Authorized the Chairman to sign the Notice of Completion; and
3. Directed the Clerk of the Board to have the Notice of Completion recorded with the County Recorder.



**RESOURCE
MANAGEMENT AGENCY
COUNTY OF TULARE
AGENDA ITEM**

BOARD OF SUPERVISORS

KUYLER CROCKER
District One

PETE VANDER POEL
District Two

AMY SHUKLIAN
District Three

J. STEVEN WORTHLEY
District Four

MIKE ENNIS
District Five

AGENDA DATE: June 26, 2018

Public Hearing Required	Yes	<input type="checkbox"/>	N/A	<input checked="" type="checkbox"/>
Scheduled Public Hearing w/Clerk	Yes	<input type="checkbox"/>	N/A	<input checked="" type="checkbox"/>
Published Notice Required	Yes	<input type="checkbox"/>	N/A	<input checked="" type="checkbox"/>
Advertised Published Notice	Yes	<input type="checkbox"/>	N/A	<input checked="" type="checkbox"/>
County Counsel Sign-Off	Yes	<input type="checkbox"/>	N/A	<input checked="" type="checkbox"/>
Meet & Confer Required	Yes	<input type="checkbox"/>	N/A	<input checked="" type="checkbox"/>
Electronic file(s) has been sent	Yes	<input checked="" type="checkbox"/>	N/A	<input type="checkbox"/>
Budget Transfer (Aud 308) attached	Yes	<input type="checkbox"/>	N/A	<input checked="" type="checkbox"/>
Personnel Resolution attached	Yes	<input type="checkbox"/>	N/A	<input checked="" type="checkbox"/>
Agreements are attached and signature line for Chairman is marked with tab(s)/flag(s)	Yes	<input type="checkbox"/>	N/A	<input checked="" type="checkbox"/>
CONTACT PERSON: Celeste Perez PHONE: (559)624-7010				

SUBJECT: Notice of Completion for Construction of the Terra Bella & Richgrove Road Improvement Project

REQUEST(S):

That the Board of Supervisors:

1. Accept the work for the construction of the Terra Bella & Richgrove Road Improvement Project as complete by Agee Construction Corporation of Clovis, California; and
2. Authorize the Chairman to sign the Notice of Completion; and
3. Direct the Clerk of the Board to have the Notice of Completion recorded with the County Recorder.

SUMMARY:

This Notice of Completion is for the construction of the Terra Bella & Richgrove Road Improvement Project. This project was completed on schedule and within the allowable budget. The work was performed by Agee Construction Corporation under Tulare County Agreement No. 28322.

This project was approved by your Board on July 18, 2017. The lowest responsible bid was submitted by Agee Construction Corporation. On August 29, 2017, your Board awarded and approved (Resolution No. 2017-0716) a contract to Agee Construction Corporation of Clovis, California in the amount of \$1,011,211.

SUBJECT: Notice of Completion for Construction of the Terra Bella & Richgrove Road Improvement Project

DATE: June 26, 2018

This project consisted of asphalt concrete road rehabilitation, pavement widening, curb & gutter, and the installation of ADA compliant curb ramps, sidewalks, and drive approaches.

There were two Contract Change Order (CCO) written for this project with a net total cost of \$16,415.26. The first CCO was written in the amount of \$2,800 to lower existing manholes prior to starting construction then raise them once construction was completed. The second CCO was written in the amount of \$13,615.26 to credit the Contractor, as set forth in the "Payment Adjustment for Price Index Fluctuations" clause of the Special Provisions, and to allow contract items to exceed the 25% threshold without the need to provide an adjustment to the contract item unit price.

An allowance of 6.24% of the contract bid amount, or \$63,060, was authorized for contingencies at the time of award setting the total approved contract amount at \$1,074,271.

The final cost to complete this project was \$1,018,455.07 which is 0.72% above the bid amount and is 5.20% below the authorized contract amount plus contingencies.

This project has been completed in accordance with the plans and specifications and is now ready for acceptance by the Board.

FISCAL IMPACT/FINANCING:

No Net County cost.

Contract Bid Amount:	\$ 1,011,211.00
6.24% of amount authorized for Contingencies	<u>\$ 63,060.00</u>
Authorized Contract Bid Amount + Contingencies	\$ 1,074,271.00
Project Cost:	\$ 1,002,039.81
Total of Contract Change Orders:	<u>\$ 16,415.26</u>
Final Project Cost:	\$ 1,018,455.07

An allowance of 6.24% of the contract bid amount, or \$63,060, was authorized for contingencies at the time of award setting the total approved contract amount at \$1,074,271.

The final project cost to complete this project was \$1,018,455.07 which is 0.72% above the bid amount and is 5.20% below the authorized contract amount plus contingencies.

This project was 100% funded through Measure R.


SUBJECT: Notice of Completion for Construction of the Terra Bella & Richgrove
Road Improvement Project

DATE: June 26, 2018

LINKAGE TO THE COUNTY OF TULARE STRATEGIC BUSINESS PLAN:

Safety and Security – This project will enhance the safety and security of the public by improving the transportation infrastructure for both the general population in the region and the motorists using this facility.

ADMINISTRATIVE SIGN-OFF:





Reed Schenke, P.E.
Director

cc: County Administrative Office

Attachment(s) Attachment A – Vicinity Map
Attachment B – Notice of Completion

**ATTACHMENT A –
VICINITY MAP**

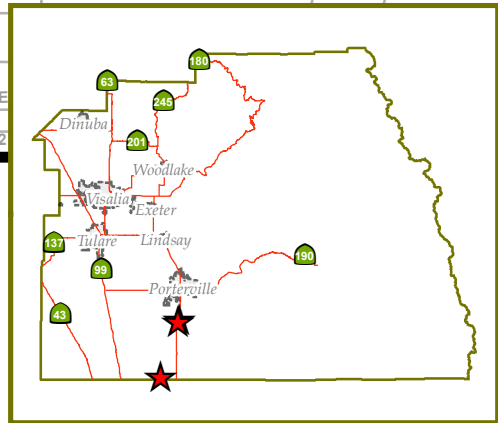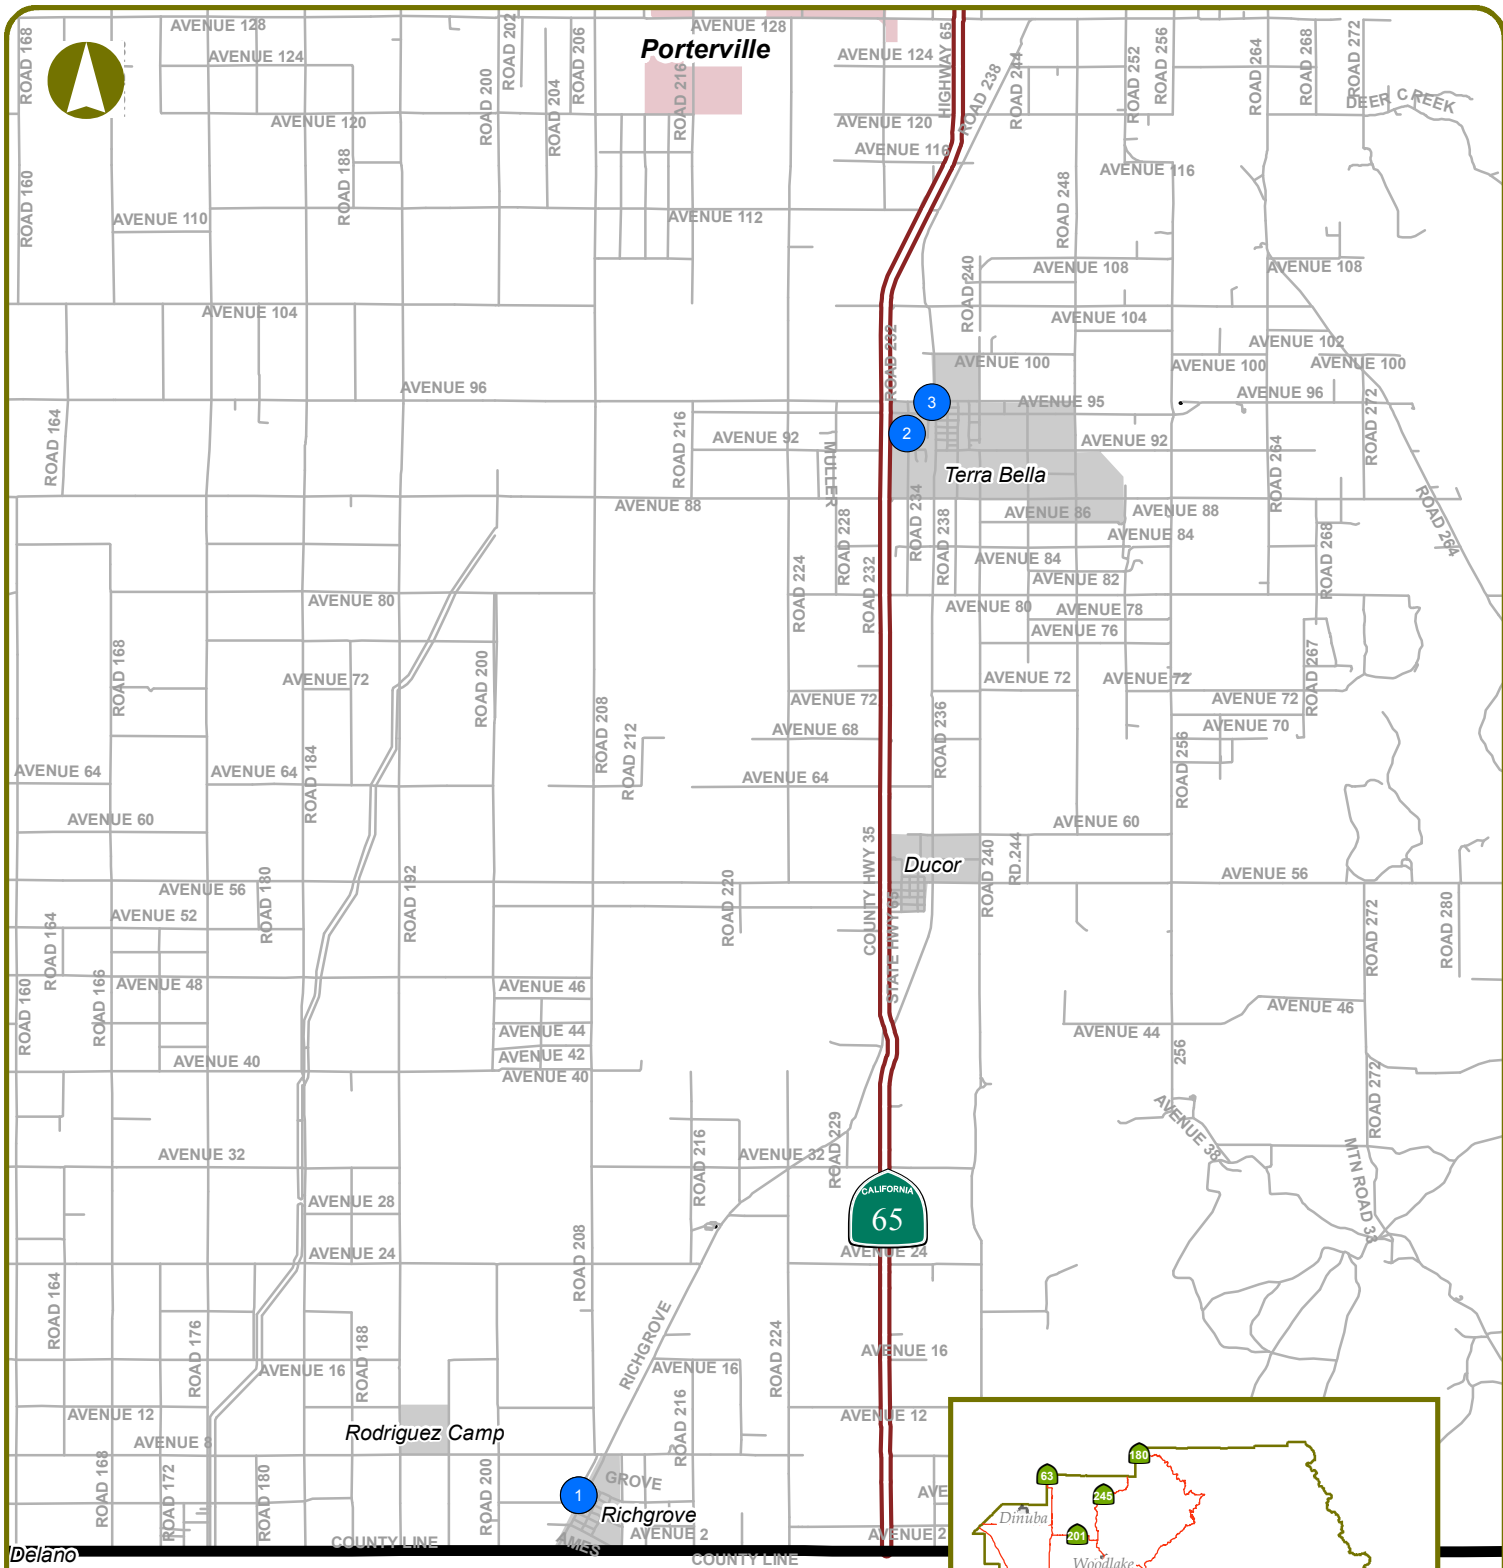

Legend

- Project Locations
- County Boundary



**ATTACHMENT B –
NOTICE OF COMPLETION**

When recorded return to:
Clerk of the Board
County of Tulare
2800 West Burrel
Visalia, CA 93291

NOTICE OF COMPLETION

NOTICE IS HEREBY GIVEN THAT:

1. The County of Tulare, a political subdivision of the State of California, is the owner of the work of improvement stated below.
2. The full address of the owner is: County of Tulare, 2800 W. Burrel Avenue, Visalia, California, 93291
3. The County of Tulare, a public agency, owns the hereinafter described work of improvement.
4. No other person(s) or corporation(s) owns any interest therein.
5. The name of the project is Terra Bella & Richgrove Road Improvement Project.
6. On the 26th day of June, 2018 the Board of Supervisors of Tulare County in Resolution Number _____ accepted as complete the work of improvement in Tulare County Agreement Number 28322 for the project identified above.
7. The name of the contractor for the work of improvement described in Tulare County Agreement Number 28322 is Agee Construction Corporation. The Contractor's address is Agee Construction Corporation, P.O. Box 629, Clovis, California, 93613.
8. The project was located in or near the communities of Terra Bella and Richgrove, County of Tulare, State of California.

The undersigned affirms that he is authorized to execute this Notice of Completion for the County of Tulare, that he has read the foregoing Notice, knows the contents hereof and that the facts stated herein are true; that he executes this Notice on behalf of and pursuant to the authorization of the Board of Supervisors of the County of Tulare.

COUNTY OF TULARE
BOARD OF SUPERVISORS

Chairman of the Board

A notary public or other officer completing this certificate verifies only the identity of the individual who signed the document to which this certificate is attached, and not the truthfulness, accuracy, or validity of that document.

State of California)
County of Tulare)

Subscribed and sworn to (or affirmed) before me on this _____ day of _____, 2018, by _____, proved to me on the basis of satisfactory evidence to be the person(s) who appeared before me.

Date: _____

Notary Signature
