



**Resource Management
Agency
COUNTY OF TULARE
AGENDA ITEM**

BOARD OF SUPERVISORS

KUYLER CROCKER
District One
PETE VANDER POEL
District Two
AMY SHUKLIAN
District Three
EDDIE VALERO
District Four
DENNIS TOWNSEND
District Five

AGENDA DATE: February 26, 2019

Public Hearing Required	Yes	<input type="checkbox"/>	N/A	<input checked="" type="checkbox"/>
Scheduled Public Hearing w/Clerk	Yes	<input type="checkbox"/>	N/A	<input checked="" type="checkbox"/>
Published Notice Required	Yes	<input type="checkbox"/>	N/A	<input checked="" type="checkbox"/>
Advertised Published Notice	Yes	<input type="checkbox"/>	N/A	<input checked="" type="checkbox"/>
Meet & Confer Required	Yes	<input type="checkbox"/>	N/A	<input checked="" type="checkbox"/>
Electronic file(s) has been sent	Yes	<input checked="" type="checkbox"/>	N/A	<input type="checkbox"/>
Budget Transfer (Aud 308) attached	Yes	<input type="checkbox"/>	N/A	<input checked="" type="checkbox"/>
Personnel Resolution attached	Yes	<input type="checkbox"/>	N/A	<input checked="" type="checkbox"/>
Agreements are attached and signature line for Chairman is marked with tab(s)/flag(s)	Yes	<input checked="" type="checkbox"/>	N/A	<input type="checkbox"/>
CONTACT PERSON: Celeste Perez PHONE: 559-624-7010				

SUBJECT: Notice of Completion for Construction of the D129 Sand Creek Bridge Project

REQUEST(S):
That the Board of Supervisors:

1. Accept the work for the construction of the D129 Sand Creek Bridge Project as complete by Agee Construction Corporation of Clovis, California; and
2. Authorize the Chairman to sign the Notice of Completion; and
3. Direct the Clerk of the Board to have the Notice of Completion recorded with the County Recorder.

SUMMARY:
This Notice of Completion is for the construction of the D129 Sand Creek Bridge Project. This project was completed on schedule and under budget. The work was performed by Agee Construction Corporation under Tulare County Agreement No. 28641.

This project was approved by your Board on April 10, 2018 (Resolution No. 2018-0236). The lowest responsible bid was submitted by Agee Construction Corporation. On June 5, 2018, your Board awarded and approved (Resolution No. 2018-0435) a contract with Agee Construction Corporation of Clovis, California in the amount of \$1,386,121.

SUBJECT: Notice of Completion for Construction of the D129 Sand Creek Bridge Project

DATE: February 26, 2019

This project consisted of replacing the existing bridge with an approximately 70-foot long by 35-foot wide, cast-in-place post-tensioned reinforced concrete voided slab bridge. The replacement bridge will accommodate two 12-ft lanes with 4-ft shoulders.

There were three Contract Change Orders (CCO) written for this project, with a net total savings to the County of \$1,732.47. The first CCO was written to credit the County in the amount of \$2,290 for substituting the pipe material used for the bridge's future utility casing. The second CCO was written in the amount of \$557.53 to compensate the Contractor as set forth in the "Payment Adjustment for Price Index Fluctuations" clause of the Special Provisions. The third CCO, zero-dollar change order, was written to eliminate two contract items of work not needed for the construction of this project and to allow contract items to go below 75% of the item bid quantity without the need to provide an adjustment to the contract item unit price.

An allowance of 5.9% of the contract bid amount, or \$81,806, was authorized for contingencies at the time of award setting the total approved contract amount at \$1,467,927.

The final project cost to complete this project was \$1,370,644.91 which is 1.12% below the bid amount and is 6.63% below the authorized contract amount plus contingencies.

This project has been completed in accordance with the plans and specifications and is now ready for acceptance by the Board.

FISCAL IMPACT/FINANCING:

No Net County Cost.

Contract Bid Amount:	\$ 1,386,121.00
5.9% of amount authorized for Contingencies:	\$ 81,806.00
Authorized Contract Bid Amount + Contingencies:	\$ 1,467,927.00
Project Cost:	\$ 1,372,377.38
Total Cost of Contract Change Orders:	\$ (1,732.47)
Final Project Cost:	\$ 1,370,644.91

An allowance of 5.9% of the contract bid amount, or \$81,806, was authorized for contingencies at the time of project approval setting the total approved contract amount at \$1,467,927.

The final project cost to complete this project was \$1,370,644.91 which is 1.12% below the bid amount and is 6.63% below the authorized contract amount plus contingencies.

This project is 100% funded by the Federal Highway Bridge Program (HBP) funds.


SUBJECT: Notice of Completion for Construction of the D129 Sand Creek Bridge Project

DATE: February 26, 2019

LINKAGE TO THE COUNTY OF TULARE STRATEGIC BUSINESS PLAN:

This project will enhance the safety and security of the public by improving the transportation infrastructure for both the general population in the region and the motorists using this facility.

ADMINISTRATIVE SIGN-OFF:



Reed Schenke, P.E.
Director

cc: County Administrative Office

Attachment(s) Attachment A – Vicinity Map
Attachment B – Notice of Completion

**BEFORE THE BOARD OF SUPERVISORS
COUNTY OF TULARE, STATE OF CALIFORNIA**

IN THE MATTER OF NOTICE OF) Resolution No. _____
COMPLETION FOR CONSTRUCTION OF)
THE D129 SAND CREEK BRIDGE)
PROJECT)

UPON MOTION OF SUPERVISOR _____, SECONDED BY
SUPERVISOR _____, THE FOLLOWING WAS ADOPTED BY THE
BOARD OF SUPERVISORS, AT AN OFFICIAL MEETING HELD FEBRUARY 26, 2019,
BY THE FOLLOWING VOTE:

AYES:
NOES:
ABSTAIN:
ABSENT:

ATTEST: JASON T. BRITT
COUNTY ADMINISTRATIVE OFFICER/
CLERK, BOARD OF SUPERVISORS



BY: _____
Deputy Clerk

* * * * *

1. Accepted the work for the construction of the D129 Sand Creek Bridge Project as complete by Agee Construction Corporation of Clovis, California; and
2. Authorized the Chairman to sign the Notice of Completion; and
3. Directed the Clerk of the Board to have the Notice of Completion recorded with the County Recorder.

Attachment A – Vicinity Map

**Road D129
Over Sand Creek Bridge**

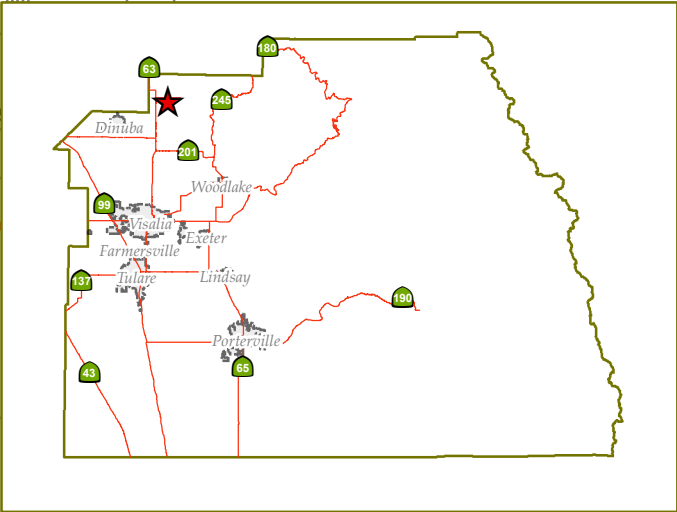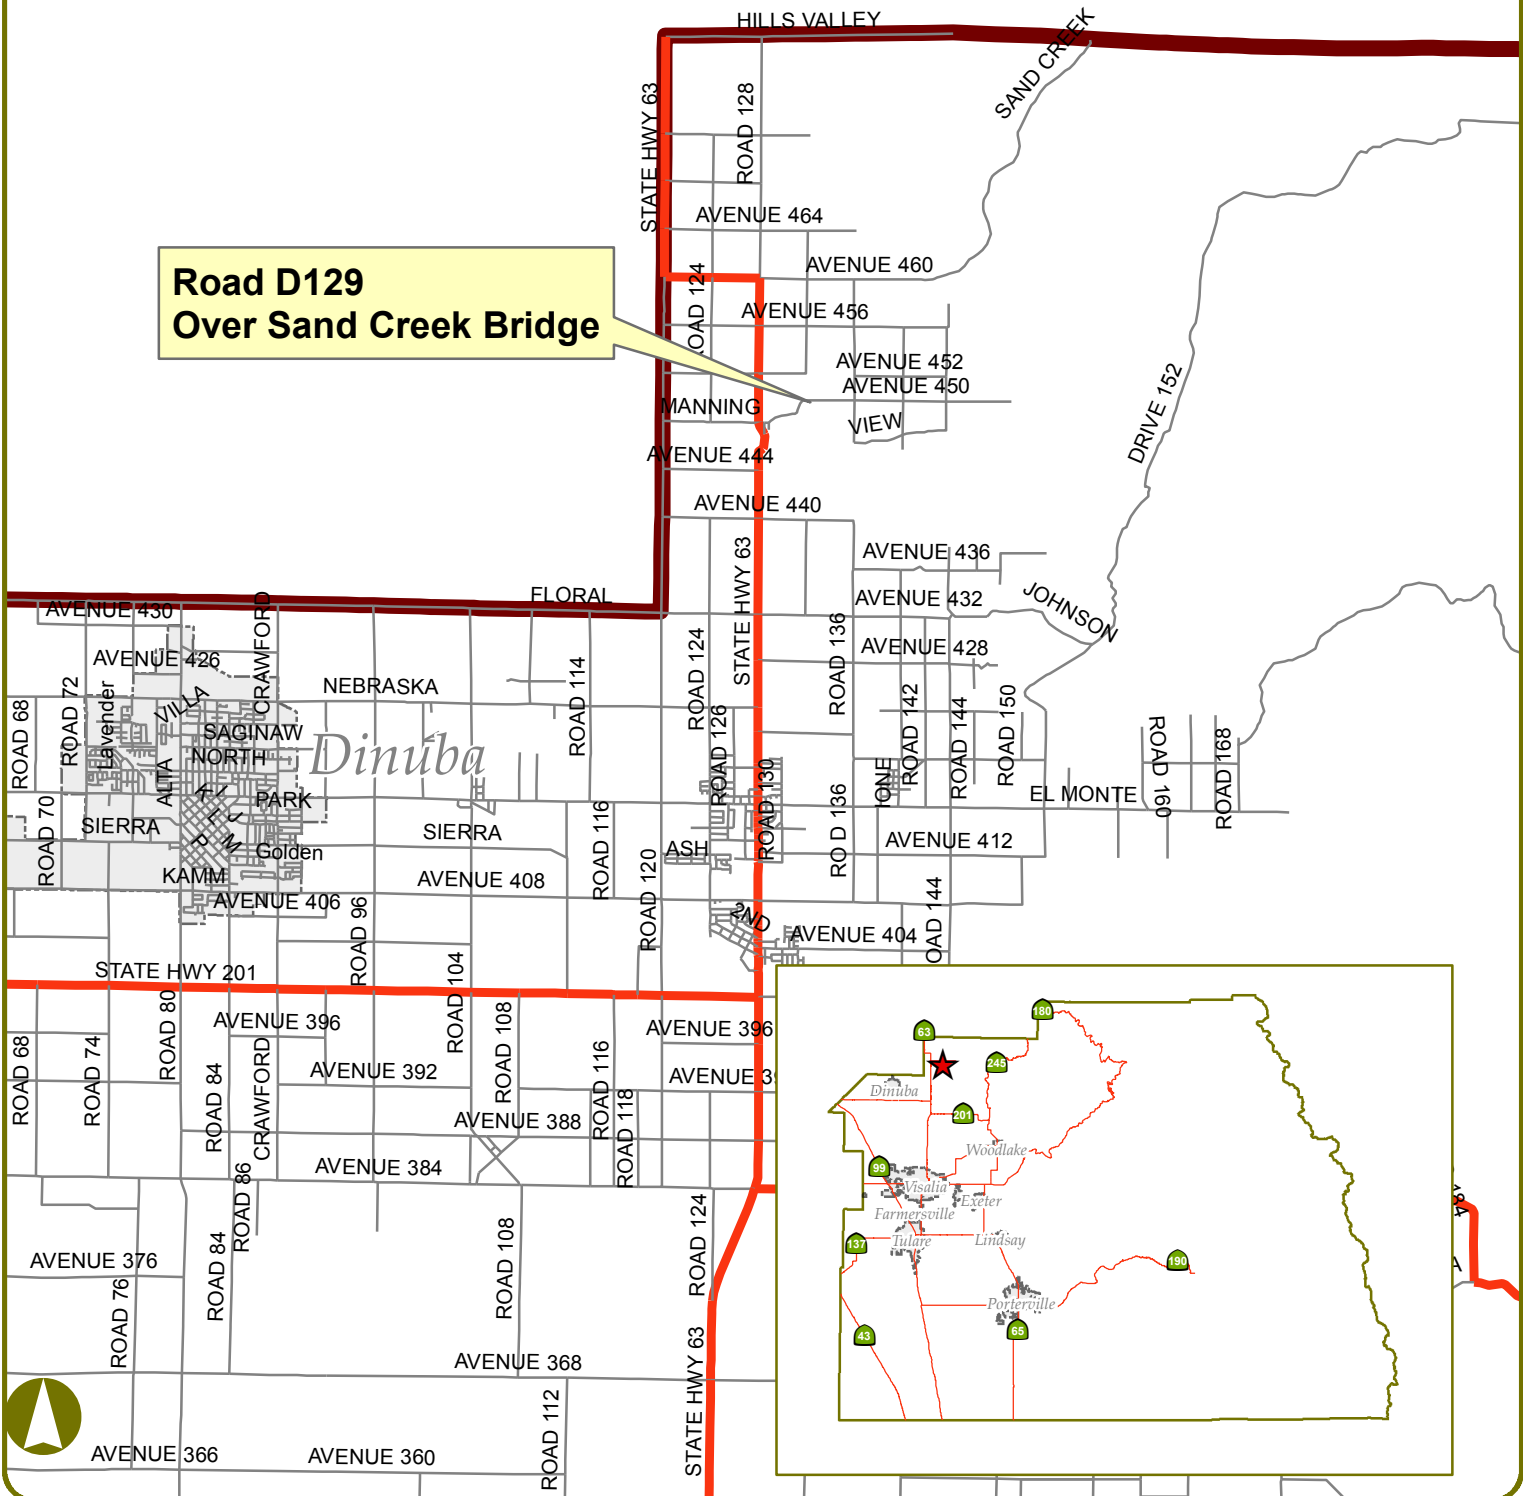

0 0.5 1 1.5 2 2.5 3
Miles

Attachment B – Notice of Completion

When recorded return to:
Clerk of the Board
County of Tulare
2800 West Burrel
Visalia, CA 93291

NOTICE OF COMPLETION

NOTICE IS HEREBY GIVEN THAT:

1. The County of Tulare, a political subdivision of the State of California, is the owner of the work of improvement stated below.
2. The full address of the owner is: County of Tulare, 2800 W. Burrel Avenue, Visalia, California, 93291
3. The County of Tulare, a public agency, owns the hereinafter described work of improvement.
4. No other person(s) or corporation(s) owns any interest therein.
5. The name of the project is D129 Sand Creek Bridge Project.
6. On the 26th day of February, 2019 the Board of Supervisors of Tulare County in Resolution Number _____ accepted as complete the work of improvement in Tulare County Agreement Number 28641 for the project identified above.
7. The name of the contractor for the work of improvement described in Tulare County Agreement Number 28641 is Agee Construction Corporation. The Contractor's address is Agee Construction Corporation, P.O. Box 629, Clovis, California, 93613.
8. The project was located on Diagonal 129 just east of State Route 63, northeast of the community of Dinuba, County of Tulare, State of California.

The undersigned affirms that he is authorized to execute this Notice of Completion for the County of Tulare, that he has read the foregoing Notice, knows the contents hereof and that the facts stated herein are true; that he executes this Notice on behalf of and pursuant to the authorization of the Board of Supervisors of the County of Tulare.

COUNTY OF TULARE
BOARD OF SUPERVISORS

Chairman of the Board

A notary public or other officer completing this certificate verifies only the identity of the individual who signed the document to which this certificate is attached, and not the truthfulness, accuracy, or validity of that document.

State of California)
County of Tulare)

Subscribed and sworn to (or affirmed) before me on this _____ day of _____, 2019, by _____, proved to me on the basis of satisfactory evidence to be the person(s) who appeared before me.

Date: _____

Notary Signature
