



**Resource Management
Agency
COUNTY OF TULARE
AGENDA ITEM**

BOARD OF SUPERVISORS

KUYLER CROCKER
District One
PETE VANDER POEL
District Two
AMY SHUKLIAN
District Three
EDDIE VALERO
District Four
DENNIS TOWNSEND
District Five

AGENDA DATE: November 5, 2019

Public Hearing Required	Yes	<input type="checkbox"/>	N/A	<input checked="" type="checkbox"/>
Scheduled Public Hearing w/Clerk	Yes	<input type="checkbox"/>	N/A	<input checked="" type="checkbox"/>
Published Notice Required	Yes	<input type="checkbox"/>	N/A	<input checked="" type="checkbox"/>
Advertised Published Notice	Yes	<input type="checkbox"/>	N/A	<input checked="" type="checkbox"/>
Meet & Confer Required	Yes	<input type="checkbox"/>	N/A	<input checked="" type="checkbox"/>
Electronic file(s) has been sent	Yes	<input checked="" type="checkbox"/>	N/A	<input type="checkbox"/>
Budget Transfer (Aud 308) attached	Yes	<input type="checkbox"/>	N/A	<input checked="" type="checkbox"/>
Personnel Resolution attached	Yes	<input type="checkbox"/>	N/A	<input checked="" type="checkbox"/>
Agreements are attached and signature line for Chairman is marked with tab(s)/flag(s)	Yes	<input type="checkbox"/>	N/A	<input checked="" type="checkbox"/>
CONTACT PERSON: Celeste Perez PHONE: (559)624-7010				

SUBJECT: Notice of Completion for Construction of Allensworth Elementary Sidewalk Improvements Project

- REQUEST(S):**
That the Board of Supervisors:
1. Accept the work for the construction of the Allensworth Elementary Sidewalk Improvements Project as complete by DOD Construction of Bakersfield, California; and
 2. Authorize the Chairman to sign the Notice of Completion; and
 3. Direct the Clerk of the Board to have the Notice of Completion recorded with the County Recorder.

SUMMARY:
This Notice of Completion is for the construction of the Allensworth Elementary Sidewalk Improvements Project. This project was completed on schedule and below the allowable budget. The work was performed by DOD Construction under Tulare County Agreement No. 28862.

This project was approved by your Board on June 26, 2018 (Resolution No. 2018-0548). The lowest responsible bid was submitted by DOD Construction. On September 25, 2018, your Board awarded and approved a contract (Resolution No. 2018-0802) to DOD Construction of Bakersfield, California in the amount of \$517,768.

This project included the installation of new sidewalk sections, curb and gutter, ADA curb ramps and drive approaches along Young Road and Avenue 36. Additionally,

SUBJECT: Notice of Completion for Construction of Allensworth Elementary Sidewalk Improvements Project

DATE: November 5, 2019

this project included flashing beacons, fencing and gate improvements, drainage improvements and pavement resurfacing.

There were three Contract Change Order (CCO) for this project with a net total cost of \$2,898.55. The first CCO was written in the amount of \$3,012.80 to compensate the Contractor for furnishing and installing a new fire hydrant assembly system. The second CCO, in the amount of zero dollars, was written to amend the project plans to reflect changes to the fencing and gate system in front of the school. The final CCO was written in the amount of \$114.25 to credit the County as set forth in the "Payment Adjustment for Price Index Fluctuations" clause.

This project has been completed in accordance with the plans and specifications and is now ready for acceptance by the Board.

FISCAL IMPACT/FINANCING:

There is No Net County cost.

Contract Bid Amount:	\$ 517,768.00
7.41% of amount authorized for Contingencies	<u>\$ 38,388.00</u>
Authorized Contract Bid Amount + Contingencies	\$ 556,156.00
Project Cost:	\$ 498,129.60
Total of Contract Changer Orders:	<u>\$ 2,898.55</u>
Final Project Cost:	\$ 501,028.15

An allowance of 7.41% of the contract bid amount, or \$38,388, was authorized for contingencies at the time of award setting the total approved contract amount at \$556,156.

The final cost to complete this project was \$501,028.15 which is 3.23% below the bid amount and is 9.91% below the authorized contract amount plus contingencies.

This project was funded through the 2017 Active Transportation Program (ATP) Augmentation and Road Funds programmed through the 2017 County Transportation Improvement Program (CTIP).


LINKAGE TO THE COUNTY OF TULARE STRATEGIC BUSINESS PLAN:

Safety and Security – This project will enhance the safety and security of the public by improving the transportation infrastructure for both the general population in the region and the motorists using this facility.

SUBJECT: Notice of Completion for Construction of Allensworth Elementary Sidewalk
Improvements Project

DATE: November 5, 2019

ADMINISTRATIVE SIGN-OFF:



Reed Schenke, P.E.
Director

cc: County Administrative Office

Attachment(s) Attachment A – Vicinity Map
Attachment B – Notice of Completion

**BEFORE THE BOARD OF SUPERVISORS
COUNTY OF TULARE, STATE OF CALIFORNIA**

IN THE MATTER OF NOTICE OF)
COMPLETION FOR CONSTRUCTION OF) Resolution No. _____
ALLENSWORTH ELEMENTARY)
SIDEWALK IMPROVEMENTS PROJECT)

UPON MOTION OF SUPERVISOR _____, SECONDED BY
SUPERVISOR _____, THE FOLLOWING WAS ADOPTED BY THE
BOARD OF SUPERVISORS, AT AN OFFICIAL MEETING HELD NOVEMBER 5, 2019,
BY THE FOLLOWING VOTE:

AYES:
NOES:
ABSTAIN:
ABSENT:

ATTEST: JASON T. BRITT
COUNTY ADMINISTRATIVE OFFICER/
CLERK, BOARD OF SUPERVISORS

BY: _____
Deputy Clerk

* * * * *

1. Accepted the work for the construction of the Allensworth Elementary Sidewalk Improvements Project as complete by DOD Construction, of Bakersfield, California; and
2. Authorized the Chairman to sign the Notice of Completion; and
3. Directed the Clerk of the Board to have the Notice of Completion recorded with the County Recorder.

**ATTACHMENT A –
VICINITY MAP**



Allensworth Elementary 

Young Rd

Avenue 39

Avenue 36




Avenue 32


Road 84

43

Burlington Way

Legend

-  Project Site
-  Project Location
-  Tulare County Boundary

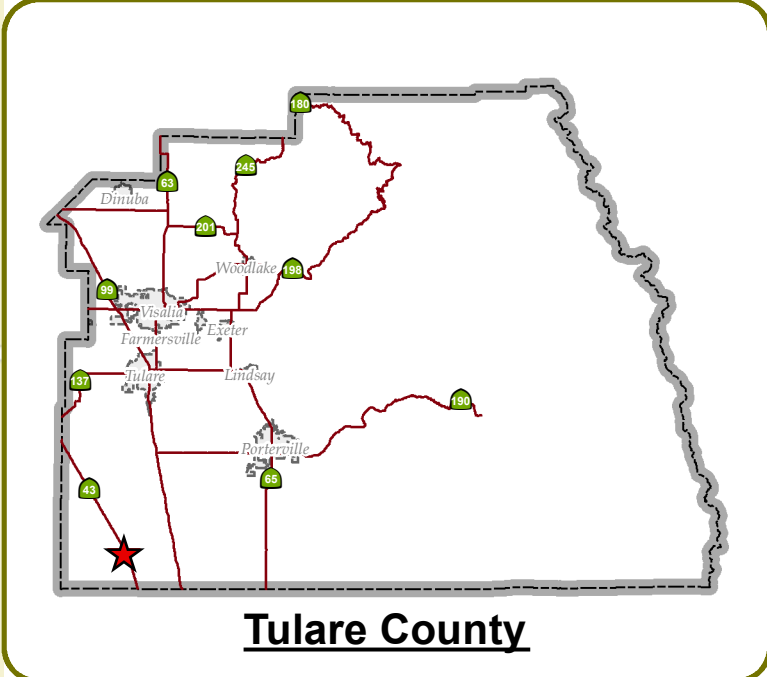

Tulare County



**ATTACHMENT B –
NOTICE OF COMPLETION**

When recorded return to:
Clerk of the Board
County of Tulare
2800 West Burrel
Visalia, CA 93291

NOTICE OF COMPLETION

NOTICE IS HEREBY GIVEN THAT:

1. The County of Tulare, a political subdivision of the State of California, is the owner of the work of improvement stated below.
2. The full address of the owner is: County of Tulare, 2800 W. Burrel Avenue, Visalia, California, 93291
3. The County of Tulare, a public agency, owns the hereinafter described work of improvement.
4. No other person(s) or corporation(s) owns any interest therein.
5. The name of the project is Allensworth Elementary Sidewalk Improvements Project.
6. On the 5th day of November, 2019 the Board of Supervisors of Tulare County in Resolution Number _____ accepted as complete the work of improvement in Tulare County Agreement Number 28862 for the project identified above.
7. The name of the Contractor for the work of improvement described in Tulare County Agreement Number 28862 is DOD Construction. The Contractor's address is DOD Construction, P.O. Box 70187, Bakersfield California, 93387.
8. The project was located in the community of Allensworth along Young Road (Road 81) and Avenue 36, County of Tulare, State of California.

The undersigned affirms that he is authorized to execute this Notice of Completion for the County of Tulare, that he has read the foregoing Notice, knows the contents hereof and that the facts stated herein are true; that he executes this Notice on behalf of and pursuant to the authorization of the Board of Supervisors of the County of Tulare.

COUNTY OF TULARE
BOARD OF SUPERVISORS

Chairman of the Board

A notary public or other officer completing this certificate verifies only the identity of the individual who signed the document to which this certificate is attached, and not the truthfulness, accuracy, or validity of that document.

State of California)
County of Tulare)

Subscribed and sworn to (or affirmed) before me on this _____ day of _____, 2019, by _____, proved to me on the basis of satisfactory evidence to be the person(s) who appeared before me.

Date: _____

Notary Signature
